



भारत सरकार
GOVT. OF INDIA

पत्तन, पोत परिवहन और जलमार्ग मंत्रालय

Ministry of Ports, Shipping & Waterways

भारतीय अन्तर्देशीय जलमार्ग प्राधिकरण

INLAND WATERWAYS AUTHORITY OF INDIA

National Waterway Road, Kannadikkadu, Maradu, Ernakulam - 682 304

Phone :- 0484 - 2389804, 2389445

E-mail :- dirkoc.iwai@nic.in

Website :- www.iwai.nic.in

No: IWAI/COCH/49/O&M-Misc/2024-25/28

Date: 28th May 2024

NOTICE INVITING QUOTATION

Inland Waterways Authority of India invites sealed quotations for " Fabrication, supply and Installation of Security Cabin at Willingdon Island Jetty, Kochi " from reputed supplier / manufacturer / fabricator, Contractor having experience in work of above-mentioned items. The details of work are as follows.

Sl. No.	Item Description	Estimated Cost (Excl. GST & Incl. Labour welfare)	EMD	Work completion period
1	<p>Fabrication, supply, and installation of security cabin at Willingdon Island Jetty, Kochi. The cabin should be as per the specifications, drawing and as per the directions of Engineer-in-charge all complete.</p> <p>Cabin floor area 1.40mtrs x1.40mtrs. Cabin height: 2.4mtrs. Doors: 1.80mtrs x 0.70mtrs x 1 nos Windows: 0.30mtrs x 0.90mtrs x 2 nos.</p> <p>Steel frame with 200x200x10mm thick base plate.</p> <p>Vertical members: 50x50x6mm MS angle.</p> <p>Intermediate ties: 32x32x3mm MS angles at 0.9mtrs and 1.80mtrs heights from floor.</p> <p>Truss roof: 2 sides slope truss using GI tube truss with 1.6mm thick members.</p> <p>Roofing material and vertical covering: 0.71mm thick Aluminium profile industrial troughed sheet of Alloy 31500/31000/40800, conforming to IS 1254, IS 737, IS 2676. The sheet shall be fixed using self-drilling/ self-tapping SS screws of size 5.5x65 mm with EPDM seal complete up to required pitch in horizontal, vertical or curved</p>	68,900.00	1500/-	20 days

Head Office:- I.W.A.I., A-13, Sector - 1, NOIDA - 210 301 (U.P.)

E-mail:- iwainoi@nic.in • Phone No:- 0120-2543972, 2543973, 2544004, 2521664, 2544036, 2522971.

Sl. No.	Item Description	Estimated Cost (Excl. GST & Incl. Labour welfare)	EMD	Work completion period
	<p>surfaces i/c cutting to size and shape where required as per specifications, detail drawings and direction of Engineer-in-Charge. The rate shall be inclusive of all screws, seal, ridge, labour, scaffolding, machinery for fixing and approved sealant where required etc. but excluding the cost of purlins, rafters and trusses</p> <p>Door shutter: GI frame with chromium plated brass butt hinges (75x65x4 mm) to cabin and 0.71mm thick aluminum troughed sheets.</p> <p>Window shutter: GI frame with chromium plated brass butt hinges (75x65x4 mm) to cabin and 1.0 mm thick polycarbonate sheet.</p> <p>Floor: 50x50x6 MS angle frame topped with 16mm thick marine chequered plywood.</p> <p>Storage box: With GI frames and 16mm thick plywood top inside the cabin.</p> <p>Painting: (two or more coats) on all structural members and fittings with epoxy enamel paint of approved brand and manufacture and required colour over a priming coat of approved epoxy steel primer on new work.</p> <p>Electrical: Light points: 2 nos, fan point: 1 nos, plug point: 1 nos. All using 1.5sqmm FRLS PVC insulated copper conductor single core cable in surface /recessed steel/PVC conduit with modular switch, modular plate, suitable GI/insulated box and earthing the point etc. complete as required as per the direction of Engineer-in-charge.</p>			

Terms & Conditions:

1. The estimated cost for the mentioned work is Rs. 68,900/- (excluding GST & Inc. Labour welfare cess @ 1%) including transportation charges and the materials should be genuine as per specifications mentioned in B.O.Q and drawing enclosed in Annex-1 and Annex-2 respectively.
2. The work will be completed within 20 days from the date of issue of this work order.
3. The payment shall be made through PFMS within 15 days after submission of bill and certification of the work by the concerned office I/C.

4. The firm should submit self-certified copy of PAN card, registration certificate of firm, GST registration number, last year ITR along with the quotation, Bank details & Cancelled cheque where payment to be made, similar work done experience certificate.
5. Firm has to submit EMD of Rs.1,500/- through RTGS/NEFT only payable in favour of "Inland Waterways Authority of India" in the A/c no. 39360627884, State Bank of India, Vyttila Branch IFSC: SBIN0008694. The scanned copy of the RTGS/NEFT receipt with transaction ID must be enclosed along with the bid.
6. The bidder shall inspect the site prior to quote the rates and submission of quotation for the above said work.
7. The quoted price shall be excluding GST as per applicable.
8. In case of delay in completion of the above work, liquidated damages will be applicable @ 1.0% per week subjected to a maximum 10% on the total value of contract.
9. 10% of bill amount (including EMD) will be withheld and will be released after completion of defect liability period of 6 months.
10. IWAI reserves the right to accept or reject any / all quotations without assigning any reason or any prior notice.

The sealed quotation should reach to IWAI, Kochi office latest by 03.06.2024 at 15.30 hrs. Any delay in receipt of quotation whatsoever will not be entertained. The received quotation will be opened on same day at 16.00 hrs.

Yours faithfully,


(A. Selvakumar)

Director

Email: aselvakumar.iwai@nic.in

Phone: 0484-2389804

Encl. 1. Annexure -1

2. Annexure -2

Copy to: 1. IWAI Website

2. Notice Board, IWAI, Kochi office.


Annexure -1

Tender Inviting Authority: Inland Waterways Authority of India, Kochi						
Name of Work: NIQ for Fabrication, supply and Installation of Security Cabin at Willingdon Island Jetty, Kochi.						
Contract No. IWAI/COCH/49/O&M-Misc/2024-25/28						
Bidder Name:						
PRICE SCHEDULE						
Sl. No.	Item Description	Item Code / Make	Qty	Units	Basic Price (in. Rs.)	Total Amount In Rs. (Col. 4x Col. 6)
1	2	3	4	5	6	7
1	<p>Fabrication, supply, and installation of security cabin at Willingdon Island Jetty, Kochi. The cabin should be as per the specifications, drawing and as per the directions of Engineer-in-charge all complete.</p> <p>Cabin floor area 1.40mtrs x1.40mtrs. Cabin height: 2.4mtrs. Doors: 1.80mtrs x 0.70mtrs x 1 nos Windows: 0.30mtrs x 0.90mtrs x 2 nos.</p> <p>Steel frame with 200x200x10mm thick base plate.</p> <p>Vertical members: 50x50x6mm MS angle.</p> <p>Intermediate ties: 32x32x3mm MS angles at 0.9mtrs and 1.80mtrs heights from floor.</p> <p>Truss roof: 2 sides slope truss using GI tube truss with 1.6mm thick members.</p> <p>Roofing material and vertical covering: 0.71mm thick Aluminium profile industrial troughed sheet of Alloy 31500/31000/40800, conforming to IS 1254, IS 737, IS 2676. The sheet shall be fixed using self-drilling/ self-tapping SS screws of size 5.5x65 mm with EPDM seal complete up to required pitch in horizontal, vertical, or curved surfaces i/c cutting to size and shape where required as per specifications,</p>	Item 1	1	Nos

Sl. No.	Item Description	Item Code / Make	Qty	Units	Basic Price (in. Rs.)	Total Amount In Rs.
	<p>detail drawings and direction of Engineer-in-Charge. The rate shall be inclusive of all screws, seal, ridge, labour, scaffolding, machinery for fixing and approved sealent where required etc. but excluding the cost of purlins, rafters and trusses.</p> <p>Door shutter: GI frame with chromium plated brass butt hinges (75x65x4 mm) to cabin and 0.71mm thick aluminum troughed sheets.</p> <p>Window shutter: GI frame with chromium plated brass butt hinges (75x65x4 mm) to cabin and 1.0 mm thick polycarbonate sheet.</p> <p>Floor: 50x50x6 MS angle frame topped with 16mm thick marine chequered plywood.</p> <p>Storage box: With GI frames and 16mm thick plywood top inside the cabin.</p> <p>Painting: (two or more coats) on all structural members and fittings with epoxy enamel paint of approved brand and manufacture and required colour over a priming coat of approved epoxy steel primer on new work.</p> <p>Electrical: Light points: 2 nos, fan point: 1 nos, plug point: 1 nos. All using 1.5sqmm FRLS PVC insulated copper conductor single core cable in surface /recessed steel/PVC conduit with modular switch, modular plate, suitable GI/insulated box and earthing the point etc. complete as required as per the direction of Engineer-in-charge.</p>					
Total Amount in Rs.					

Signature and seal of contractor.

Installation of Security Cabin for Security guard at Willingdon Island Jetty

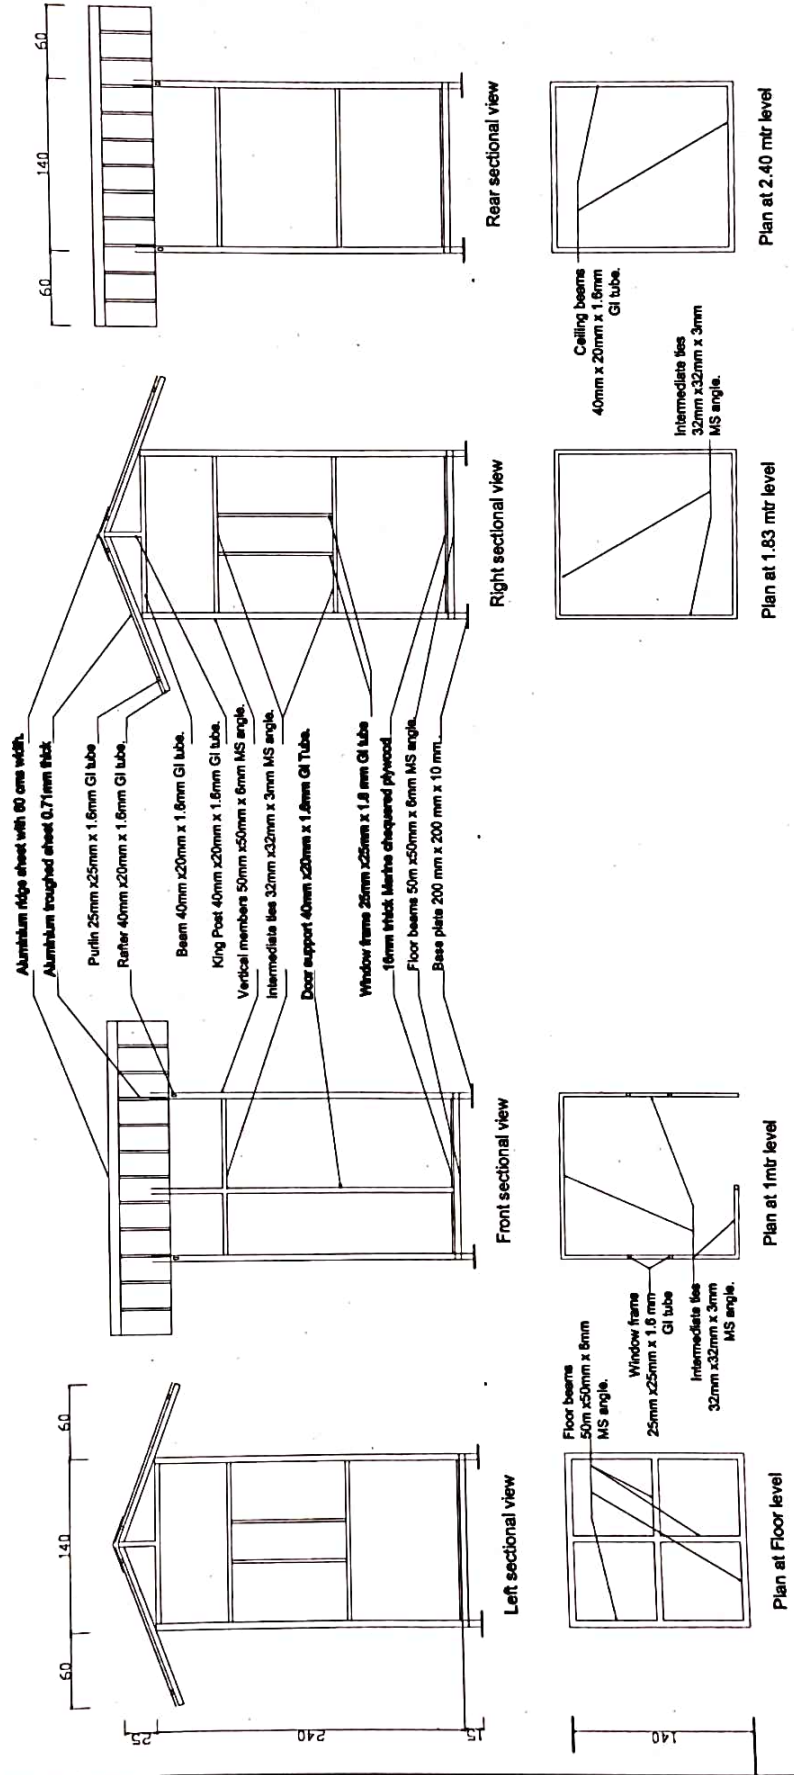

1. All dimensions are in centimeters unless otherwise specified.
2. The all sides of the cabin shall be covered with 0.71mm thick aluminum sheets.
3. Window shutters will be of Polycarbonate transparent sheet with GI tube frame (25mm x 25mm x 1.6mm thick).
4. Door shutters will be of 0.71mm thick aluminum sheets and GI tube frame (25mm x 25mm x 1.6mm thick).
